

**SOUND LEVEL MEASUREMENT**

DATE : 19 JAN 2007

KVA 3125 HZ 60 COOLING SYSTEM :-> RADIATOR

WORK ORDER : SO13088 GEN. SERIAL No: 2132365


ENGINE MODEL : mtu 20V4000

ENGINE SERIAL No : 528 100 413

ATERNATOR MODEL : LSA54 L8-4P

ATERNATOR SERIAL No : 601271 / 1

ENGINE SPEED : 1800 RPM

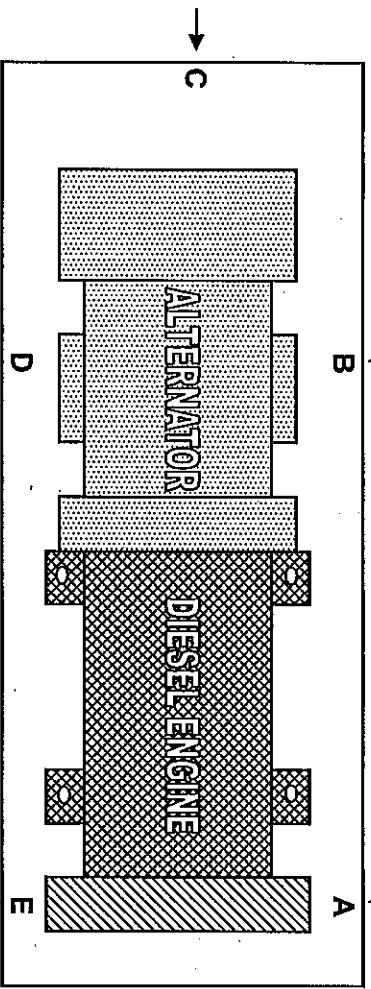

ALL READINGS TO BE TAKEN AT 1 METRE AWAY FROM GENERATOR SET

LOAD % ->	No Load (db)	100% ( dB )	Remark
POSITION A	110.8	115.2	
POSITION B	109.4	114.3	
POSITION C	105.2	112.4	
POSITION D	108.7	118.2	
POSITION E	109.3	115.5	

Test By : E.S.TAY Witnessed By : CT CI

Signature : [Signature] Signature : T.M. Kao

